

SUMMARY

100 Rock Mull, Peachtree City, GA 30269 Lauren Gleaton May 28, 2022







3.1.1 Siding, Flashing & Trim SIDING - SEAL OPENING(S) REAR

Recommend sealing the opening(s) in the exterior siding to prevent moisture, insect and vermin intrusion.

Recommendation Contact a qualified professional.





3.1.2 Siding, Flashing & Trim TRIM - LOOSE

LEFT

Loose trim observed in one or more locations. Recommend this be addressed as needed.

Recommendation Contact a qualified professional.





3.1.3 Siding, Flashing & Trim **TRIM - RECOMMEND PAINTING WOOD TRIM** FRONT

Recommend painting wood trim to extend wood life.





3.1.4 Siding, Flashing & Trim TRIM - VINYL TRIM DAMAGE

Contact a qualified professional.

Recommendations

3.1.5 Siding, Flashing & Trim VENT COVER(S) - DAMAGED

REAR

repaired.

Recommendation

One or more vent covers were damaged on exterior walls. Recommend they be repaired or replaced as needed.

Cracked/damaged vinyl trim was observed. Recommend it be

Recommendation Contact a qualified professional.





3.2.1 Exterior Doors DOORFRAME - DECAYED WOOD REAR



Decayed wood doorframe and door noted at one or more exterior doors. Recommend a qualified contractor evaluate and address as needed.



3.3.1 Walkways & Driveways DRIVEWAY - CRACKING (MINOR)

Recommendations

Minor cosmetic cracks observed, which may indicate movement in the soil. Recommend monitor and/or have concrete contractor patch/seal.

Recommendation

Contact a qualified concrete contractor.



3.3.2 Walkways & Driveways WALKWAY - TRIP HAZARD (UPHEAVAL)

Upheaval noted in walkway. Recommend repairs for safety.

Recommendation Contact a qualified concrete contractor.





3.6.1 Vegetation, Grading, Drainage & Retaining Walls **GRADING - (4-6) INCHES OF SEPARATION** RIGHT / REAR



Typically, 4-6 inches of separation between the siding and earth is recommended for both moisture and termite control reasons. Several areas of the foundation perimeter should be addressed to meet this desired separation.

Recommendation Contact a qualified professional.



3.6.2 Vegetation, Grading, Drainage & Retaining Walls TREE - DEBRIS ON ROOF

- Recommendations

Tree debris observed on roof. This can cause improper drainage to gutters and downspouts. Recommend clearing debris.

Recommendation Contact a handyman or DIY project



3.6.3 Vegetation, Grading, Drainage & Retaining Walls **TREE - OVERHANG/PROXIMITY**



FRONT / RIGHT

Tree(s) observed in close proximity to the residence and/or overhanging the roof. Trees can cause damage to the roof/residence and prevent proper drainage. Recommend a qualified tree service address as necessary.

Recommendation Contact a qualified tree service company.



3.6.4 Vegetation, Grading, Drainage & Retaining Walls

VEGETATION - DIRECT CONTACT FRONT

Vegetation in direct contact with the residence should be trimmed back for moisture, insect control and security reasons.

Recommendation Contact a qualified landscaping contractor





4.5.1 Garage Door Opener **SAFETY SENSORS - BYPASSED**

Safety sensors for the automatic garage door have been bypassed. Recommend this be addressed for safety.

Recommendation Contact a qualified garage door contractor.

4.6.1 Occupant Door (From Garage To Inside Of Home) **DOOR - DID NOT MEET SEPARATION**


REQUIREMENTS

Although, this was acceptable at time of construction, the interior door separating the garage and home does not meet current safety standards. Doors in this type of location (firewalls) must be at least 1 3/8-inch thick, metal/steel, or a 20-minute fire-rated door.

Additionally the door was missing weatherstripping. Recommend the door be replaced for fire safety reasons.

Recommendation Contact a handyman or DIY project Safety Hazards





5.2.1 Roof Drainage (Gutters & Downspouts) SPLASHBLOCKS OR DOWNSPOUT **EXTENSIONS - NOT PRESENT**

RIGHT REAR

Recommend splashblocks or downspout extensions to better divert water away from the foundation.

Recommendation Contact a handyman or DIY project

45 minutes

5 minutes

25 seconds

5 seconds

2 seconds

1 second

Sept. 15, 197

6.5.1 Water Heaters, Controls, Flues & Vents WATER TEMPERATURE

Time for 1st Degree

(normal shower temp.) (pain threshold)

35 minutes

1 minute

5 seconds

2 seconds

1 second

instantaneous

dum, C.P.S.C., Pe

Water heater should operate between 120 degrees Fahrenheit (to supply adequately heated water for dishwasher) and a maximum of 130 degrees Fahrenheit (for safety/scalding reasons). Address as needed.

Recommendation **Recommended DIY Project**

Table 10.2 Scald chart Water Temperatu °F (°C)

04-110 (43.3)

116 (46.7 116 (46.7)

122 (50)

131 (55)

140 (60)

149 (65

154 (67 8 (U.S. Government N

,	
7 1 1 Service Entrance	

.1.1 Service Entrance **GROUND STAKE - RAISED**

The entire electrical system is connected to the ground stake (outside near the power meter). In order for ground stakes to provide the best connection to earth, they must be driven flush with the ground. The ground stake was not flush and should be addressed.

Recommendation Contact a qualified electrical contractor.

7.2.1 Main & Subpanels, Service & Grounding, Main Overcurrent Device LUGGING - EXCESSIVE

Current electrical practices have determined excessive lugging can cause poor and loose connections. Only a single neutral is currently permitted under each lug. Three ground connections are currently allowed under a single lug. Recommend evaluation by an electrician to determine if repair is warranted.

Recommendation Contact a qualified electrical contractor.















Recommendations

Safety Hazards

7.2.2 Main & Subpanels, Service & Grounding, Main Overcurrent Device SLOT - OPEN



Open slot in main electrical panel is allowing immediate access to live voltage and may present a hazard to small children. Recommend a blank cover be installed for safety's sake.

Recommendation Contact a qualified professional.



7.4.1 Lighting Fixtures, Switches & Receptacles ELECTRICAL RECEPTACLE(S) - INOPERABLE

MULTIPLE LOCATIONS

One or more electrical receptacles were found to be inoperable at time of inspection. Receptacles did not appear to be tied to a wall switch and breakers were on at time of inspection. Recommend a qualified contractor evaluate and address as needed.

Recommendation

Contact a qualified electrical contractor.



Master Bedroom



2nd Floor Front Center Bedroom

7.4.2 Lighting Fixtures, Switches & Receptacles JUNCTION BOX - MISSING (LOOSE WIRE CONNECTION)

ATTIC

Observed one or more wiring splices that were not enclosed within properly rated junction box. Recommend a junction box be installed to properly contain the wire connection by a qualified professional.

Recommendation Contact a qualified electrical contractor.





7.5.1 GFCI & AFCI RECEPTACLES - NOT TIED TO A GFCI

KITCHEN

One or more electrical outlets were in GFCI required areas but did not appear to be tied to a GFCI circuit. Recommend a qualified contractor evaluate and address as needed.



Recommendation Contact a qualified electrical contractor.





7.6.1 Smoke Detectors CHIRPING

Chirping smoke detectors noted at time of inspection. Address as needed for safety's sake.

Recommendation Contact a qualified professional.





7.6.2 Smoke Detectors **LOW BATTERY**Smoke detector failed to respond when tested. Recommend battery
be replaced.
Recommendation
Contact a handyman or DIY project



7.7.1 Carbon Monoxide Detectors C/O DETECTOR - LOW BATTERY



Carbon monoxide detector failed to respond when tested. Recommend battery be replaced.



9.3.1 Sink(s) DRAIN PIPE - LEAK



Water leak noted on drain pipe for master bath sink. Recommend a qualified contractor evaluate and address as needed.

Recommendation Contact a qualified plumbing contractor.



9.6.1 Tub/Shower GROUT - SEPARATIONS



Separations noted in grout in the master bathroom tub/shower. Recommend maintenance to ensure water tightness.



9.6.2 Tub/Shower TUB SPOUT - SEAL



There was a gap between the tub spout and the shower wall that can allow moisture to get behind the shower wall. Recommend it be sealed to prevent moisture intrusion into the wall.

Recommendation Contact a qualified professional.

10.3.1 Sink(s) DRAIN PIPE - LEAK

Water leak noted on drain pipe for guest bath sink. Recommend a qualified contractor evaluate and address as needed.

Recommendation

Contact a qualified plumbing contractor.



1st Floor 1/2 Bath

2nd Floor Guest Bathroom

10.6.1 Tub/Shower TUB SPOUT - SEAL

There was a gap between the tub spout and the shower wall that can allow moisture to get behind the shower wall. Recommend it be sealed to prevent moisture intrusion into the wall.

Recommendation Contact a qualified professional.



10.6.2 Tub/Shower TUB/SHOWER - DAMAGE OBSERVED

Visible damage observed in the tub (missing bar). Recommend a qualified contractor evaluate and address as needed







10.6.3 Tub/Shower TUB/SHOWER DIVERTER - FAILURE TO FULLY CONVERT

Water control valve for the guest bath tub/shower would not fully convert to the shower mode and should be addressed as needed.

Recommendation Contact a qualified plumbing contractor.



11.1.1 Doors DOOR - MISSING MULTIPLE LOCATIONS



One or more doors were missing at time of inspection. Recommend they be replaced.

Recommendation Contact a qualified professional.



11.2.1 Windows WINDOW EGRESS - REASONABLE FORCE



KITCHEN / LIVING ROOM

Unable to open one or more window(s) using reasonable force. This is considered to be a safety concern due to emergency egress. Recommend all windows be repaired/exercised and verified for proper operation prior to move closing.



11.2.2 Windows WINDOW(S) - FINISH FAILING

GARAGE

Finish was failing on one or more wood windows. Recommend they be sanded and refinished to extend wood life.

Recommendation Contact a qualified professional.





11.3.1 Floors FLOORING - DAMAGED

2ND FLOOR FRONT RIGHT BEDROOM

The home had general moderate damage visible at the time of the inspection. Recommend service by a qualified contractor.



11.3.2 Floors SUB FLOOR - NOISE

2ND FLOOR FRONT CENTER BEDROOM

Sub floor noise was noticed in various areas of the home. This is common in homes of this age. Recommend adding additional hardware if the floor coverings are ever removed.

Recommendation Contact a qualified professional.





11.3.3 Floors **TILE(S) - LOOSE** 2ND FLOOR GUEST BATHROOM



Loose tiles are present at time of inspection. Recommend a qualified contractor re-attach and seal.

11.4.1 Walls DRYWALL - DAMAGED

2ND FLOOR FRONT RIGHT BEDROOM / LIVING ROOM


Damaged drywall observed in one or more locations. Recommend it be repaired as needed.

Recommendation Contact a qualified professional.

11.4.2 Walls WALL - DOORKNOB HOLE

2ND FLOOR FRONT RIGHT BEDROOM

Wall had damage from doorknob. Recommend a qualified handyman or drywall contractor repair.

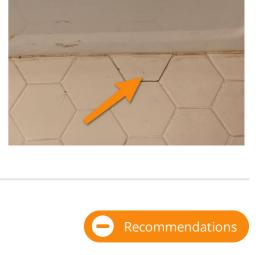





11.5.1 Ceilings CEILING - DAMAGE (MINOR)

MASTER BATHROOM / LIVING ROOM

Minor damage or deterioration to the ceiling was visible at the time of the inspection. Address as necessary.

Recommendation Contact a qualified professional.



11.5.2 Ceilings DISCOLORATION/STAIN(S) - DRY

Recommendations

One or more areas of discoloration/staining observed on the ceiling were tested with an electronic moisture meter and were found to be dry at the time of the inspection. The client is encouraged to monitor this location and address as needed. Client may wish to paint these areas.

Recommendation Recommend monitoring.



12.2.1 Sink(s) P-TRAP - NOT VISIBLE

Kitchen sink drain does not appear to have a P-Trap installed. P-Traps prevent sewer gasses from emerging into the home. Recommend a qualified contractor evaluate and address as needed.

Recommendation Contact a qualified plumbing contractor.



12.5.1 Range/Oven/Cooktop/Vent ANTI-TIP BRACKET - MISSING



Unsecured ranges may tip forward if excessive weight or pressure is applied to open door/racks. Recommend installation of an anti-tip bracket on the rear side of the kitchen stove for safety's sake.

Recommendation Contact a handyman or DIY project



13.1.1 Fireplace DAMPER CLAMP - MISSING



Recommend installation of a damper clamp for the fireplace gas logs for safety's sake.

Recommendation Contact a qualified chimney contractor.



13.1.2 Fireplace GAS PIPE PENETRATION - SEAL



Separations observed around gas entrance pipe at fireplace. Recommend this be properly sealed in order contain flames and excess heat inside firebox.

Recommendation Contact a qualified professional.



13.1.3 Fireplace PILOT LIGHT - WOULD NOT IGNITE

The fireplace was inoperative. Pilot light would not ignite. Recommend a qualified contractor evaluate and address as needed.





14.1.1 Access ATTIC PULL-DOWN STAIRS/DOOR -**NOT INSULATED**

Recommend insulation and weatherstripping for the attic pull-down stairs and/or door for energy efficiency.

Recommendation Contact a qualified professional.

14.1.2 Access Safety Hazards **ATTIC PULL DOWN STAIRS - TOO LONG**

Attic pull down attic stairs were too long and caused the steps to bow in the middle. Recommend they be cut to the appropriate size for safety's sake.

Recommendation Contact a qualified professional.

14.2.1 Attic Insulation **INSULATION - DISTURBED/LOW SECTIONS**

Disturbed/low sections of attic insulation may cause hot/cold spots directly below. Recommend these areas be addressed by adding and evenly distributing the insulation. Recommended level is 10-13 inches.

Recommendation

Contact a qualified insulation contractor.











14.2.2 Attic Insulation INSULATION - INSUFFICIENT



Insulation depth was inadequate. Recommend a qualified attic insulation contractor install additional insulation. Recommended level is 10-13 inches.

Recommendation Contact a qualified insulation contractor.



14.4.1 Moisture/Damage Concerns BATHROOM FAN(S) - DISCHARGE IN ATTIC

Recommendations

Bathroom fans currently terminate directly in the attic. Recommend they be routed to the exterior to prevent moisture damage.

